

Terminal Upgrade Project

Example Engineering | Client: Example Client | Bonny Terminal

WEEKLY PROJECT PROGRESS REPORT

PCR-0007

GENERATED ON DEMAND

REPORTING PERIOD

06 Aug 2026 - 12 Aug 2026

PROGRESS OVERVIEW

Project health and delivery completion

Needs attention

PROJECT HEALTH

25%

DELIVERY COMPLETION

+5%

MOVEMENT THIS WEEK

20

PLANNED DELIVERABLES

5

ISSUED

2

OVERDUE

PROJECT CONTEXT

Project Brief

PROJECT INTRODUCTION

Upgrade the terminal systems and issue controlled engineering deliverables.

KEY OBJECTIVES

- Complete design reviews
- Issue approved deliverables

DISCIPLINE PERFORMANCE

Lifetime scope, weekly delivery and cumulative position

DISCIPLINE	TOTAL MDR	SUBMITTED TO DATE	PLANNED THIS WEEK	ISSUED THIS WEEK	WEEKLY VARIANCE	PROJECT VARIANCE	PLAN COMPLETION	ACTUAL COMPLETION
Process	10	3	2	1	-1	-2	50%	30%
Mechanical	10	2	1	1	0	-2	40%	20%

Weekly variance = issued this week minus planned this week. Project variance = submitted to date minus the cumulative MDR plan due by the report cut-off.

PAST WEEK

Delivery activity

2

ISSUED THIS WEEK

5

TOTAL ISSUED

4

DELIVERABLES DUE

Completion movement is +5%. The project maintained or improved its issued-deliverable position.

NEXT WEEK LOOK-AHEAD

Planned deliverable submissions

PROCESS			1 DELIVERABLE
PLANNED DATE	DOCUMENT	RESPONSIBLE	REQUIRED ISSUE
15 Aug 2026	PRJ-PRO-001 - Process design basis	Process team	Issued for review

CHALLENGES AND ACTIONS

Open project issues requiring attention


HIGH

Vendor data pending
Required pump data has not been received.
Owner: Project Engineer | Target: 18 Aug 2026

SCHEDULE PERFORMANCE

Project delivery S-curve

Cumulative planned and actual progress as percentages of total MDR deliverables against project dates.

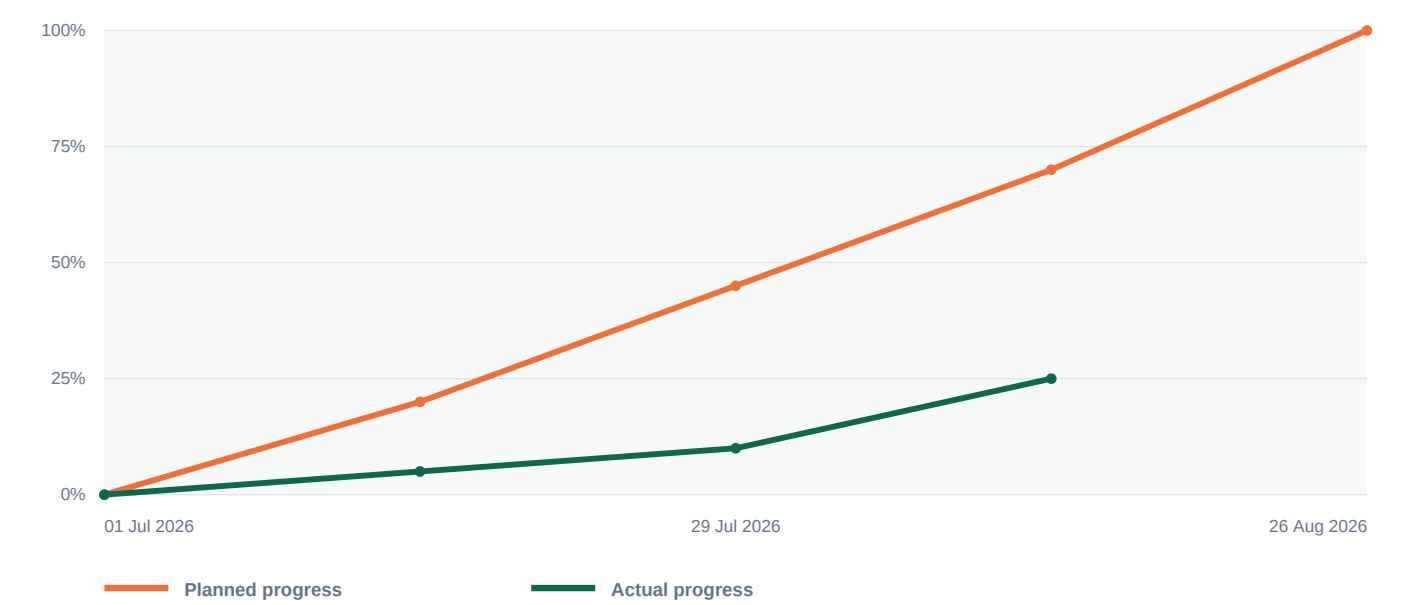

DISCIPLINE	PLANNED	ISSUED	VARIANCE	COMPLETION
Mechanical	10	2	-8	20%
Process	10	3	-7	30%
